



BTR Riverside Shanghai – design impression



ANG Hangzhou – design impression

Banyan Tree Holdings Limited

2Q10 Project Progress Report


FORWARD LOOKING STATEMENTS

This document is provided to you for information only and should not be relied on or used as a basis for making any specific investment, business or commercial decision. No representation or warranty, expressed or implied, is made as to, and no reliance should be placed on, the information or opinions contained herein. This document does not constitute and should not be construed as, any offer or solicitation for the subscription, purchase or sale of any securities of Banyan Tree Holdings Limited ("Banyan Tree"). Nothing in this document should be construed as a recommendation regarding the securities of Banyan Tree.

Certain statements in this document may constitute "forward-looking statements", including statements regarding, amongst other things, Banyan Tree's business and growth strategy. These statements reflect Banyan Tree's expectations and are subject to risks and uncertainties that may cause actual results to differ materially and may adversely affect the outcome and financial effects of the plans described herein. You are cautioned not to rely on such forward-looking statements. Banyan Tree disclaims any obligation to update their view of such risks and uncertainties or to publicly announce the result of any revisions to the forward-looking statements made herein, except where they would be required to do so under applicable law.

Banyan Tree is under no obligation to keep current the information contained in this document and any opinions expressed in it are subject to change without notice. None of Banyan Tree or any of its affiliates, advisers or representatives shall have any liability whatsoever for any loss whatsoever arising from any use of this document or its contents, or otherwise arising in connection with this document (whether direct, indirect, consequential or other). This document is not intended to provide professional advice and should not be relied upon in that regard. Prospective investors should consult their tax, legal, accounting or other advisers.

The information in this document is given in confidence and reproduction of this document, in whole or in part, or disclosure of any of its contents, without prior consent of Banyan Tree, is prohibited. This document remains the property of Banyan Tree and on request must be returned and any copies destroyed.

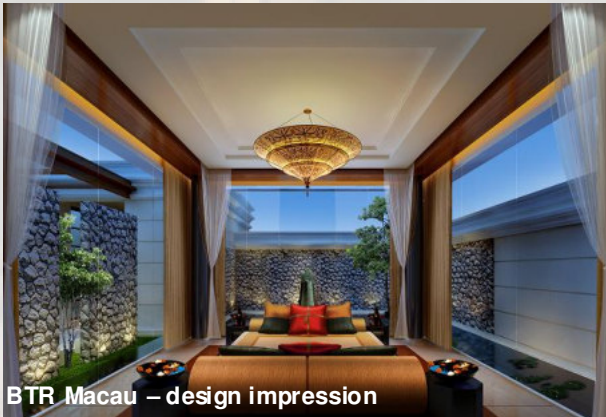

AGENDA

1. Executive Brief

2. Project Completion Schedule

Executive Brief

The purpose of this quarterly report is to update our shareholders on the progress of new projects targeted to open within the next 24 months from now. The current target completion/opening of these resorts and progress status is compared to the last quarter's announced date.


Summary

- ❖ We have soft opened Banyan Tree Club & Spa Seoul, South Korea in June 2010 and Banyan Tree Samui, Koh Samui, Thailand in July 2010.
- ❖ In 2010, we anticipate 2 new openings which we are constantly monitoring.
- ❖ We have moved Banyan Tree Beijing, China to removed project as it is in the process of being terminated.








PROJECT COMPLETION SCHEDULE 2010

NO	Resorts/Hotels <u>Without</u> Equity Interest	Status of Project	Current Completion/ Opening	Progress Status	Third Party Owner Delay	BTH Delay	Remarks
	 Angsana						
1.	Hangzhou, China	62% Construction	2010				
2.	Fu Xian Lake, Yunnan, China	85% Construction	2010				

Note: Project Progress Status is compared to the last quarter announced date.




-  **Progress on track**
-  **On track, but might be delayed (3 to 6 months) pending some issues**
-  **Delayed (more than 6 months), see attached Delayed Project Report**



PROJECT COMPLETION SCHEDULE 2011

NO	Resorts/Hotels <u>Without</u> Equity Interest	Status of Project	Current Completion/ Opening	Progress Status	Third Party Owner Delay	BTH Delay	Remarks
	<u>Banyan Tree</u>						
1.	Macau, China	40% Construction	2011				
2.	Kerala, India	20% Construction	2011				
3.	Riverside Shanghai, China	50% Construction	2011				

Note: Project Progress Status is compared to the last quarter announced date.

-  **Progress on track**
-  **On track, but might be delayed (3 to 6 months) pending some issues**
-  **Delayed (more than 6 months), see attached Delayed Project Report**



PROJECT COMPLETION SCHEDULE 2011

NO	Resorts/Hotels <u>Without</u> Equity Interest	Status of Project	Current Completion/ Opening	Progress Status	Third Party Owner Delay	BTH Delay	Remarks
	 <u>Angsana</u>						
1.	Baladava, Mauritius	60% Construction	2011				
2.	Eastern Mangrove, Abu Dhabi, UAE	60% Construction	2011				

Note: Project Progress Status is compared to the last quarter announced date.

- Progress on track**
- On track, but might be delayed (3 to 6 months) pending some issues**
- Delayed (more than 6 months), see attached Delayed Project Report**



PROJECT COMPLETION SCHEDULE 2012


NO	Resorts/Hotels <u>With</u> Minority Equity Interest	Status of Project	Current Completion/ Opening	Progress Status	Third Party Owner Delay	BTH Delay	Remarks
	<u>Banyan Tree</u>						
1.	Hue, Vietnam	Construction	2012				

Note: Project Progress Status is compared to the last quarter announced date.

- Progress on track**
- On track, but might be delayed (3 to 6 months) pending some issues**
- Delayed (more than 6 months), see attached Delayed Project Report**



PROJECT COMPLETION SCHEDULE 2012

NO	Resorts/Hotels <u>Without Equity Interest</u>	Status of Project	Current Completion / Opening	Progress Status	Third Party Owner Delay	BTH Delay	Remarks
	<u>Banyan Tree</u>						
1.	North Bund, Shanghai, China	Under construction	2012				

Note: Project Progress Status is compared to the last quarter announced date.

- Progress on track**
- On track, but might be delayed (3 to 6 months) pending some issues**
- Delayed (more than 6 months), see attached Delayed Project Report**



PROJECT COMPLETION SCHEDULE 2012

NO	Resorts/Hotels <u>With</u> Minority Equity Interest	Status of Project	Current Completion/ Opening	Progress Status	Third Party Owner Delay	BTH Delay	Remarks
	 Angsana						
1.	Lijiang, China	Design completed	2012	/			Pending China Fund
2.	Lhasa, Tibet, China	Design stage	2012	/			Pending China Fund
3.	Hue, Vietnam	Construction	2012				


Note: Project Progress Status is compared to the last quarter announced date.

- Progress on track**
- On track, but might be delayed (3 to 6 months) pending some issues**
- Delayed (more than 6 months), see attached Delayed Project Report**



PROJECT COMPLETION SCHEDULE

Removed projects

NO	Resorts/Hotels <u>Without</u> Equity Interest	Third Party Owner Issue	BTH Issue	Remarks
	<u>Banyan Tree</u>			
1.	Beijing, China	√		In the process of termination



BTR Riverside Shanghai – design impression



ANG Hangzhou – design impression

THANK YOU
