



ANG Hangzhou – design impression



BTR Macau – design impression

## **Banyan Tree Holdings Limited**

### **4Q10 Project Progress Report**


# FORWARD LOOKING STATEMENTS

This document is provided to you for information only and should not be relied on or used as a basis for making any specific investment, business or commercial decision. No representation or warranty, expressed or implied, is made as to, and no reliance should be placed on, the information or opinions contained herein. This document does not constitute and should not be construed as, any offer or solicitation for the subscription, purchase or sale of any securities of Banyan Tree Holdings Limited ("Banyan Tree"). Nothing in this document should be construed as a recommendation regarding the securities of Banyan Tree.

Certain statements in this document may constitute "forward-looking statements", including statements regarding, amongst other things, Banyan Tree's business and growth strategy. These statements reflect Banyan Tree's expectations and are subject to risks and uncertainties that may cause actual results to differ materially and may adversely affect the outcome and financial effects of the plans described herein. You are cautioned not to rely on such forward-looking statements. Banyan Tree disclaims any obligation to update their view of such risks and uncertainties or to publicly announce the result of any revisions to the forward-looking statements made herein, except where they would be required to do so under applicable law.

Banyan Tree is under no obligation to keep current the information contained in this document and any opinions expressed in it are subject to change without notice. None of Banyan Tree or any of its affiliates, advisers or representatives shall have any liability whatsoever for any loss whatsoever arising from any use of this document or its contents, or otherwise arising in connection with this document (whether direct, indirect, consequential or other). This document is not intended to provide professional advice and should not be relied upon in that regard. Prospective investors should consult their tax, legal, accounting or other advisers.

The information in this document is given in confidence and reproduction of this document, in whole or in part, or disclosure of any of its contents, without prior consent of Banyan Tree, is prohibited. This document remains the property of Banyan Tree and on request must be returned and any copies destroyed.

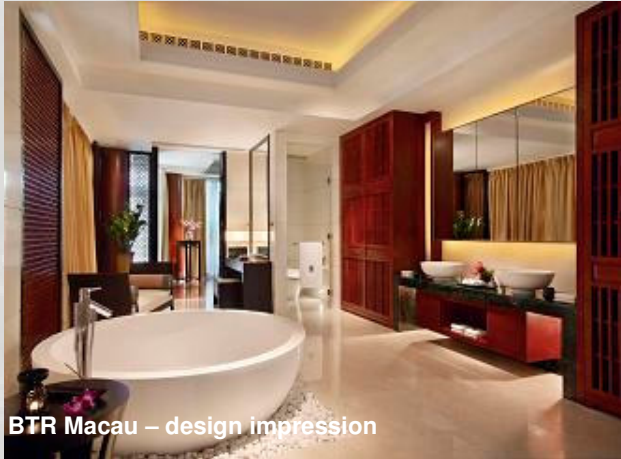

# AGENDA

1. Executive Brief

2. Project Completion Schedule

# Executive Brief



The purpose of this quarterly report is to update our shareholders on the progress of new projects targeted to open within the next 24 months from now. The current target completion/opening of these resorts and progress status is compared to the last quarter's announced date.

## Summary

- ❖ Banyan Tree Kerala's opening date has been delayed to 2012 due to slow construction progress.
- ❖ We have added Banyan Tree Alqueva, Maura, Portugal which is slated to open by 4<sup>th</sup> quarter of 2012.
- ❖ The list in 2013 is only for those projects spilled over from 2012.



# PROJECT COMPLETION SCHEDULE 2011

NO	Resorts/Hotels <u>Without</u> Equity Interest	Status of Project	Current Completion/ Opening	Progress Status	Third Party Owner Delay	BTH Delay	Remarks
	 <b><u>Banyan Tree</u></b>						
1.	Macau, China	80% Construction	2011				
2.	Riverside Shanghai, China	57% Construction	2011				
	 <b><u>Angsana</u></b>						
1.	Balaclava, Mauritius	70% Construction	2011				
2.	Hangzhou, China	68% Construction	2011				

*Note: Project Progress Status is compared to the last quarter announced date.*

	<b>Progress on track</b>
	<b>On track, but might be delayed (3 to 6 months) pending some issues</b>
	<b>Delayed (more than 6 months), see attached Delayed Project Report</b>



# PROJECT COMPLETION SCHEDULE 2012


NO	Resorts/Hotels <u>With</u> Minority Equity Interest	Status of Project	Current Completion/ Opening	Progress Status	Third Party Owner Delay	BTH Delay	Remarks
	 <b><u>Banyan Tree</u></b>						
1.	Lang Co, Hue, Vietnam	7% Construction	2012				
	 <b><u>Angsana</u></b>						
1.	Lang Co, Hue, Vietnam	10% Construction	2012				

*Note: Project Progress Status is compared to the last quarter announced date.*

- Progress on track**
- On track, but might be delayed (3 to 6 months) pending some issues**
- Delayed (more than 6 months), see attached Delayed Project Report**



# PROJECT COMPLETION SCHEDULE 2012


NO	Resorts/Hotels <u>Without Equity Interest</u>	Status of Project	Current Completion / Opening	Progress Status	Third Party Owner Delay	BTH Delay	Remarks
	<b><u>Banyan Tree</u></b>						
1.	North Bund, Shanghai, China	Sub-structure	2012				
2.	Tianjin, China	50% Construction & ID Design Stage	2012				
3.	Kerala, India	30% Construction	2012		√		Slow construction progress
4.	Alqueva, Maura, Portugal	Design stage	2012				
5.	Jiuzhaigou, China	Design stage	2012				

*Note: Project Progress Status is compared to the last quarter announced date.*

- Progress on track**
- On track, but might be delayed (3 to 6 months) pending some issues**
- Delayed (more than 6 months), see attached Delayed Project Report**



# PROJECT COMPLETION SCHEDULE 2013

NO	Resorts/Hotels <u>With</u> Minority Equity Interest	Status of Project	Current Completion/ Opening	Progress Status	Third Party Owner Delay	BTH Delay	Remarks
	 <u>Angsana</u>						
1.	Lhasa, Tibet, China	Design stage	2013				

*Note: Project Progress Status is compared to the last quarter announced date.*

- Progress on track*
- On track, but might be delayed (3 to 6 months) pending some issues*
- Delayed (more than 6 months), see attached Delayed Project Report*





ANG Hangzhou – design impression



BTR Macau – design impression

# THANK YOU
